

BHRUHAT BANGALORE MAHANAGARA PALIKE**FORM OF PROPOSAL FOR GRANTING EXTENTION OF TIME**

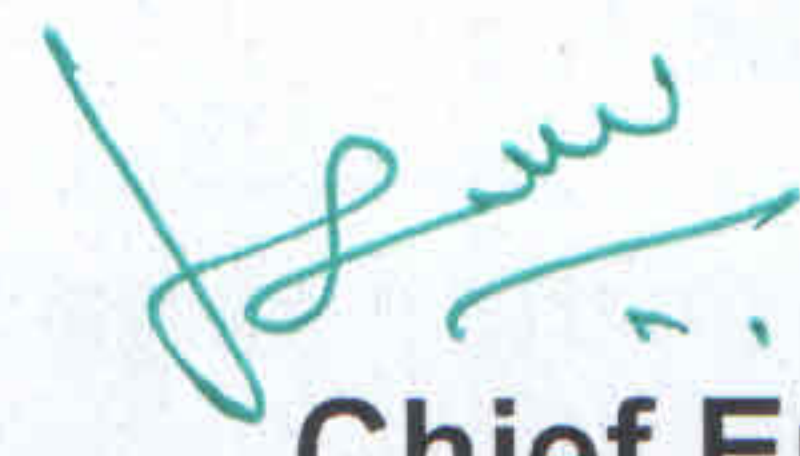
1	Name Of Work	Providing and Fixing of street light and other Street lighting accessories in Ward No-3
2	Estimate cost / amount	2.00 Lakhs
3	Name Of Contractor	M/s Sri Lakshmi Varadaraja Electrical Stroes
4	Amount of Contractor	Rs. 1,49,071.00
5	Agreement No.	EE/Ele/YZ/AGR/ 02/2013-14, Dt:03-08-2013
6	No. and date Under which the work order has been issued	EE/Ele/YZ/WO/02/2013-14, Dt:03-08-2013
7	Time limit originally fixed for completion	02-09-2013
8	Date of application by the contractor for granting extension	22-08-2013
9	Date of receipt of application in the sub-division office	23-08-2013
10	Extension granted if any	YES
	1. Form	
	2. Form	
11	Work Carriedout by the contractor during the original period stipulated in contract	51
12	Work carried out during the first period of extension	55%
13	Work carried out during And extension	100%
14	Time now applied for	
15	Date of recommending time limit applied	23-08-2013
16	Wheather the original application of contractor is enclosed	Yes
17	Balance work remaining to be done	Nil

18	Probable time required for completion of remaining work	Nil
19	Cost of work charged establishment charge on the work after the expiry of original period	Nil
20	Whether the notice as per clause has been issued	
21	Report by Asst. Executive engineer	
22	Recommendation of executive engineer	


Asst. Engineer BBMP


Asst. Executive Engineer
BBMP Yelahanka Zone


Executive Engineer
BBMP Yelahanka Zone


Chief Engineer
BBMP Yelahanka Zone
